

Project Planning Phase
Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	28 July 2026
Name	Shaik Mobeen Arfath
Project Name	Automated Network Request Management in ServiceNow
Maximum Marks	5 Marks

1. Product Backlog, Sprint Schedule, and Estimation

Use the below table to define the product backlog, story point estimations, and sprint assignments:

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Catalog Item & Form Validation	USN-1	As a requester, I want to submit network requests with dynamic IPv4 validation on the Service Portal.	5	High	Developer 1

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-1	Approval Workflow Governance	USN-2	As an approver, I want to receive email notifications with 1-click approval buttons for fast processing.	5	High	Developer 2
Sprint-1	Task Orchestration	USN-3	As a network engineer, I want auto-generated sc_task records pre-populated with target IP variables.	5	High	Developer 1
Sprint-1	CMDB & SLA Integration	USN-4	As an admin, I want completed requests to auto-update target CMDB records and enforce 8h/24h SLAs.	5	High	Developer 2
Sprint-2	Executive Analytics	USN-5	As a manager, I want Performance Analytics dashboards to track active request volume and MTTR trends.	8	Medium	Developer 1

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority	Team Members
Sprint-2	Automated Provisioning	USN-6	As an admin, I want IntegrationHub REST/SSH spokes to auto-configure target switch interfaces.	12	Low	Developer 2

2. Project Tracker, Velocity & Burndown Chart

Project Tracker Table

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	20	10 Days	17 Jun 2026	26 Jun 2026	20	26 Jun 2026

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-2	20	10 Days	27 Jun 2026	06 Jul 2026	20	06 Jul 2026
Sprint-3	20	10 Days	07 Jul 2026	16 Jul 2026	20	16 Jul 2026
Sprint-4	20	10 Days	17 Jul 2026	26 Jul 2026	20	26 Jul 2026

Velocity Calculation

With a 10-day sprint duration and a team capacity velocity of 20 story points per sprint, the team's average velocity (*AV*) per iteration unit (story points completed per day) is calculated as:


$$AV = \frac{\text{Velocity}}{\text{Sprint Duration}} = \frac{20}{10} = 2 \text{ story points / day}$$

Burndown Chart Concept & Metrics

A **Burndown Chart** provides a daily visual comparison between actual work remaining versus ideal planned progress:

- **Y-Axis (Total Effort):** Remaining story points for the sprint (starting at 20 points).
- **X-Axis (Time):** Days elapsed during the iteration (Day 1 through Day 10).
- **Ideal Line:** A linear trend line burning down steadily by 2 story points per day until reaching 0 on Day 10.
- **Actual Line:** Tracks daily completed user stories to identify bottlenecks early and ensure full delivery by the sprint end date[cite:4].

Sprint Burndown Chart: Sprint-4 (Jul 17 – Jul 26, 2026)

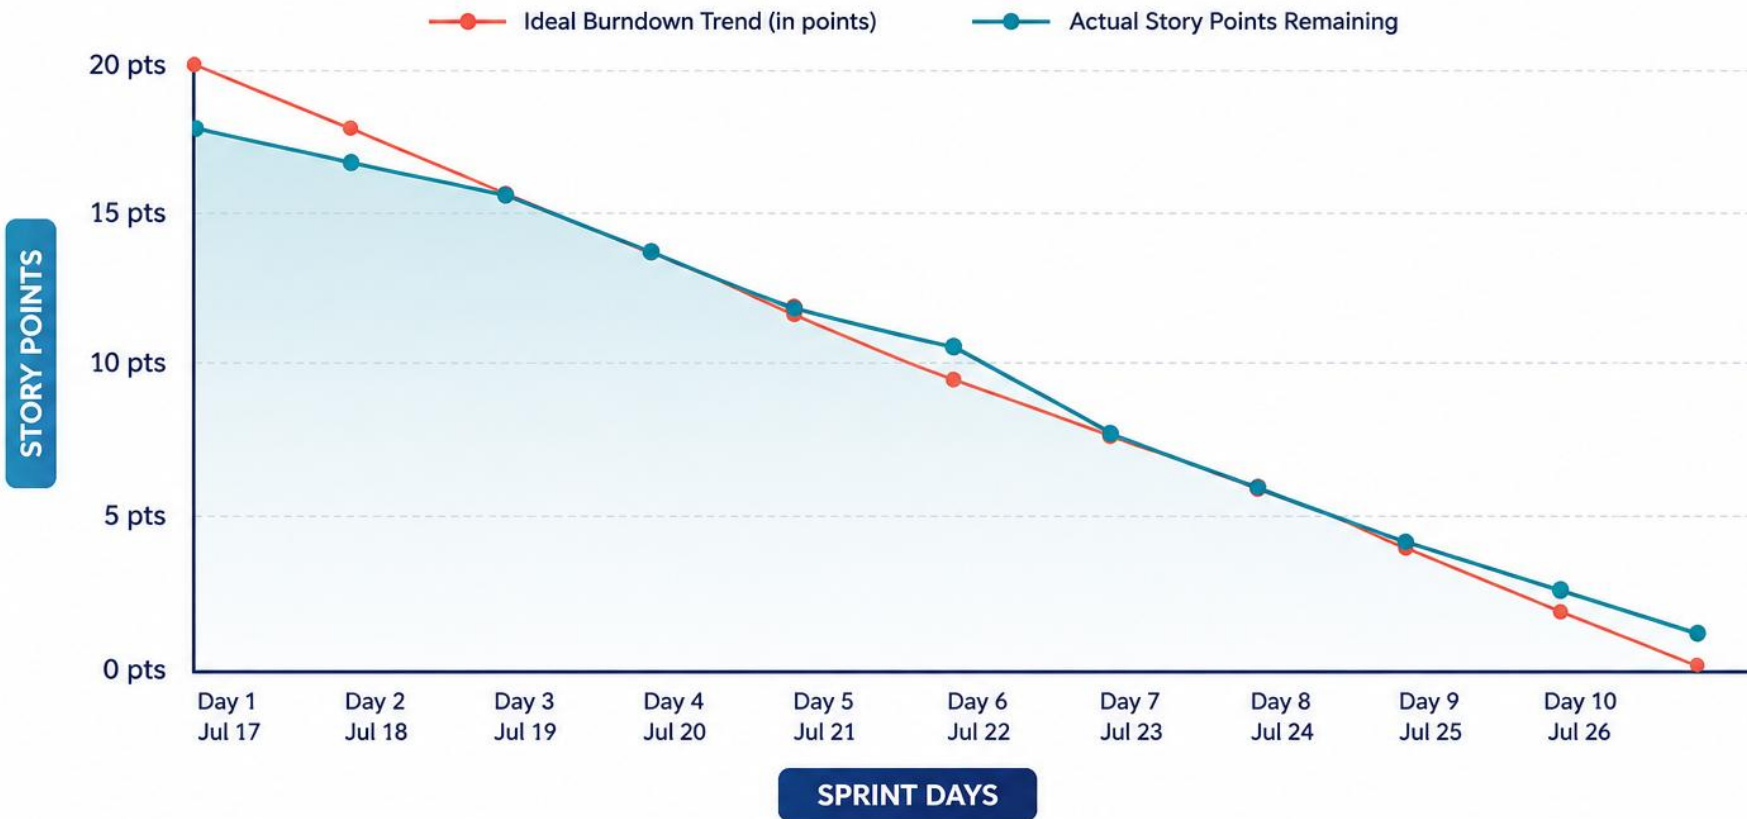

Total Scope
20 Story Points



Sprint Duration
10 Days



Average Velocity
2 Points / Day



End Date (Goal)
26 July 2026
